

Town of Lincoln

Summary Report

Beamsville Water Distribution System and Jordan-Vineland Water Distribution System

JANUARY 1, 2025 – DECEMBER 31, 2025

Preamble

This report was prepared by the Director, Public Works, and Manager, Regulatory Compliance, for the Owner of the Beamsville Water Distribution System and Jordan/Vineland System, the Corporation of the Town of Lincoln, to be presented to Council at the Committee of the Whole meeting on June 22, 2026.



Table of Contents

1. **GLOSSARY** 4
2. **PURPOSE** 5
3. **SYSTEM OVERVIEW** 6
4. **LEGISLATIVE COMPLIANCE** 7
   - Water Quality Testing 7
   - Adverse Water Quality Incidents 10
   - MECP Drinking Water System Inspection Report 10
   - Regulatory Updates 10
   - Training and Competency 11
5. **FLOW AND LOSS DATA** 12
   - Flow Data 12
   - Loss Data 14
6. **INFRASTRUCTURE** 16
   - Capital Projects and Purchases 16
   - Rehabilitation and Repairs 16
   - Frozen Water Services 18
   - Booster Pumping Stations 18
7. **REGION OF NIAGARA – SUPPLY** 19
   - Master Servicing Plan 19
   - DWQMS/Compliance Working Group 19
   - Memorandums of Understanding 19
8. **MONITORING AND IMPROVEMENT INITIATIVES** 20
   - Backflow Prevention 20
   - Monitoring Program for Lower Residual Areas 20
   - Focused Water Quality Monitoring 21
   - Smart Hydrant Technology and Leak Detection 21
   - Water Meter Program 21
   - Ontario One-Call 21
9. **STAFFING** 22
   - License Renewals 22
   - License Upgrades 23
   - Operator-In-Charge Designation 23
10. **MUNICIPAL DRINKING WATER LICENSING PROGRAM** 24
11. **QUALITY MANAGEMENT SYSTEM** 25
    - Infrastructure Review 25
    - Management Review 26
12. **SPOTLIGHT ON 2026** 28
    - Capital Projects 28
    - Water Quality 28
    - DWQMS 28
    - Staffing 28
    - Asset Management Plan 28
    - Growth & Looking Forward 29

APPENDIX A
Beamsville Water Distribution System Annual Report

APPENDIX B
Jordan/Vineland Water Distribution System Annual Report

APPENDIX C
DWQMS Certification of Accreditation

1. Glossary

DWQMS	Drinking Water Quality Management Standard
EA	Environmental Assessment
MECP	Ontario Ministry of the Environment, Conservations and Parks
OIC	Operator-in-Charge, as per Ontario Regulation 128/04
OIT	Operator-in-Training, as per Ontario Regulation 128/04
ORO	Overall Responsible Operator, as per Ontario Regulation 128/04
QMS	Quality Management System
WTP	Water Treatment Plant





2. Purpose



For each water system, two annual water reports are required by the Ministry of the Environment, Conservations and Parks (MECP) to be prepared – the 'MECP Annual Report' (O. Reg. 170/03 section 11), and the municipal 'Summary Report' (O. Reg. 170/03 schedule 22).

The MECP Annual Reports for 2025 have been prepared and are attached as Appendix A and B for Council approval. Once approved by Council they will be made available to the public via the internet or for viewing and pick up at Town Hall.

This summary report is the compilation of the MECP Annual Reports for both the Beamsville and Jordan-Vineland Water Distribution Systems.

As legislated, Council is responsible as Owner of the water systems for ensuring these reports are prepared and available to the public (before February 28, 2026, for the 2025 MECP Annual Report).

To enhance the communication and understanding of both reports, this Annual Waterworks Summary Report contains additional non-legislated information on the drinking water system operations and water quality.





3. System Overview

The provision of drinking water for residents in Niagara region is a responsibility shared between two tiers of municipal government. The Niagara Region is responsible for treatment and supply of the water to the Town of Lincoln via transmission mains. The Town of Lincoln is responsible for distributing water to local consumers via its own network of distribution pipes.

Beamsville

The Town of Lincoln renewed the license (#067-102) and permit (#067-202) to operate the Beamsville Distribution System in Jan. 2025.

The Beamsville Water Distribution System is classified as a Class 2 Water Distribution Subsystem and services municipal residents in the Beamsville area. The distribution system services approximately 16,000 consumers. The system receives its supply of treated water from a transmission main from the Niagara Region's Grimsby Water Treatment Facility located in the Town of Grimsby. The Niagara Region owns and operates a pressure booster station located in Grimsby near the Town of Lincoln border and a storage reservoir located at the south limit of Hixon Street. Water is re-chlorinated as it enters the Town and as it leaves the Hixon Street reservoir. The Niagara Region owns and operates a small booster pumping station serving the Edelheim Road area (pressure Zone 3) located in the most southern portion the of the distribution system.

The Town owned system infrastructure consists of approximately:

- 65 kilometers of watermain
  - > 150mm to 400mm diameter
  - > PVC, cast iron, re-lined cast iron, ductile iron, asbestos cement and polyethylene
- 456 fire hydrants
- 556 valves
- 16 pressure reducing valve chambers
- 1 booster pumping station equipped with a backup diesel generator. (pressure Zone 2)
- 1 bulk water filling station located at Town Hall.

Jordan-Vineland

The Town of Lincoln renewed the license (#067-101) and permit (#067-201) to operate the Jordan-Vineland Distribution System in Jan. 2025.

The Jordan-Vineland Water Distribution System is classified as a Class 2 Water Distribution Subsystem and services municipal residents in the urban hamlets of Vineland, Jordan, Jordan Station and Prudhommes. The distribution system services approximately 7,600 consumers. The system receives its supply of treated water from a transmission main from the Niagara Region's Decew Water Treatment Facility located in the City of St. Catharines. The Niagara Region owns and operates a pressure booster station located at the most easterly boundary of Lincoln, and a storage reservoir located on Fifth Avenue at Victoria Avenue, just south of Vineland. Water is re-chlorinated at each of these locations.

The Town owned system infrastructure consists of approximately:

- 42 kilometers of watermain
  - > 100m to 300mm diameter
  - > PVC, cast iron, re-lined cast iron, ductile iron, asbestos cement and polyethylene
- 256 fire hydrants
- 266 valves
- 2 pressure reducing valve chambers
- 2 booster pumping stations.

4. Legislative Compliance

Water Quality Testing

Ontario Regulation 170/03 prescribes water quality testing requirements for municipal drinking water systems.

The requirements prescribed by the MECP include testing parameters, number of test samples, frequency of testing, location of testing, reporting of test results, and reporting and corrective action of adverse test results amongst other items. Operational guidelines are parameters used to monitor the general quality of water and the performance of the system.

The Town carried out testing in 2025 as prescribed by legislation.

The Town was granted relief under Schedule 15.1 of Ontario Regulation 170/03 in December 2009. The Town is no longer required to take samples from residential or non-residential plumbing for the community lead testing program; however, reduced sampling must still take place in four locations within the distribution system on a three-year cycle. These samples are tested for: pH, alkalinity and lead. As such, the Town has continued with its lead testing program in the distribution system under the relief regime as required, with no concerns.

In addition to the prescribed sampling, the Town tested for water quality in response to complaints from consumers. Complaints generally refer to color, odor, pressure, particulate, supply and/or taste. Testing may also be performed as a proactive approach to diagnose and monitor water quality trends.

Beamsville

The Town promptly responded and resolved **2** water quality/supply complaints for the Beamsville system in 2025.

- Two were related to taste and odour.
- None were related to pressure.
- None were related to frozen services.

Jordan-Vineland

The Town promptly responded and resolved **1** complaint for the Jordan-Vineland system in 2025.

- None were related to taste and odour.
- One was related to pressure.
- None were related to frozen services.

Taste and odour episodes are usually related to a natural phenomenon caused by seasonal biological changes in the source water. These changes may produce odor-causing chemical compounds that can be detected by humans at very low levels. Most municipalities in Ontario which obtain their water supply from surface water sources experience this problem periodically in the summer or early fall.

The Niagara Region Water Treatment Plants are equipped with various filtration systems designed to reduce the effects of taste and odour but may not eliminate it entirely.

Table 1 shows the testing requirements and number of deficient samples in 2025 for Beamsville.

Table 2 shows the testing requirements and number of deficient samples in 2025 for Jordan-Vineland.

Table 3 shows the summary of all tests performed in both systems during 2025.

*A summary of the tests performed by the Town's licensed Operators can be found in **Appendix A and Appendix B**.*

Table 1 – 2025 Testing Summaries for Beamsville System

Parameter	**# Samples Required**	**Actual # Samples Taken**	**Legislated Requirement**	**Guideline**	**Actual # Samples Exceeding Limit** (not including resamples)
Escherichia Coli (bacteriological)	24 per month	~ 30 per month (7 per week)	Not detected - 0 CFU/100mL	--	None
Total Coliform (bacteriological)	24 per month	~ 30 per month (7 per week)	Not detected - 0 CFU/100mL	--	None
HPC (heterotrophic plate count - bacteriological)	6 per month (25% of 24)	~ 30 per month (7 per week)	--	< 500 CFU/100mL (AWWA C651-05)	None
Background population (bacteriological)	Not required	~ 30 per month (7 per week)	--	<200 CFU/100mL (former O.G.)	None
Trihalomethanes	1 per quarter	1 per quarter	100 ug/L (annual running average)	--	None
Free chlorine	7 per week	10 per week	>=0.05 mg/L, <=4.0 mg/L	--	None
pH	4 per semi-annual test period	4 per semi-annual test period	--	6.5 – 8.5 O.G.	None *(see comment in MECP Summary report)*
Alkalinity	4 per semi-annual test period	4 per semi-annual test period	--	30 – 500 mg/L O.G.	None
Lead	4 per applicable semi-annual test period, 8 per applicable year of test cycle	4 per applicable semi-annual test period, 8 per applicable year of test cycle	0.01 mg/L	--	None

O.G. – operational guideline

Table 2 – 2025 Testing Summary for Jordan-Vineland System

Parameter	# Samples Required	Actual # Samples Taken	Legislated Requirement	Guideline	Actual # Samples Exceeding Limit (not including resamples)
Escherichia Coli (bacteriological)	16 per month	~ 21 per month (5 per week)	Not detected - 0 CFU/100mL	--	None
Total Coliform (bacteriological)	16 per month	~ 21 per month (5 per week)	Not detected - 0 CFU/100mL	--	None
HPC (heterotrophic plate count - bacteriological)	4 per month (25% of 16)	~ 21 per month (5 per week)	--	< 500 CFU/100mL (AWWA C651-05)	None
Background population (bacteriological)	Not required	~ 21 per month (5 per week)	--	<200 CFU/100mL (former O.G.)	None
Trihalomethanes	1 per quarter	1 per quarter	100 ug/L (annual running average)	--	None
Free chlorine	7 per week	8 per week	>=0.05 mg/L, <=4.0 mg/L	--	None
pH	3 per semi-annual test period	3 per semi-annual test period	--	6.5 – 8.5 O.G.	None *(see comment in MECP Summary report)*
Alkalinity	3 per semi-annual test period	3 per semi-annual test period	--	30 – 500 mg/L O.G.	None
Lead	3 per applicable semi-annual test period, 6 per applicable year of test cycle	3 per applicable semi-annual test period, 6 per applicable year of test cycle	0.01 mg/L	--	None

O.G. – operational guideline

Table 3 – 2025 Testing Summary for the Beamsville and Jordan/Vineland Systems

System	Regular	Maintenance	Commission	THM	HAA	Lead	Chlorine	Total
Beamsville	488	2	81	4	4	8	~609	1196
Jordan/Vineland	293	0	45	4	4	8	~477	831
Total	781	2	126	8	8	16	1086	2027

Adverse Water Quality Incidents

An "adverse water quality incident" refers to a water quality test result exceeding the legislated requirements shown in Table 1 and 2 above.

Beamsville

There were no incidents of adverse water quality conditions detected in the system for 2025 from the regular sampling schedule.

Jordan-Vineland

There were no incidents of adverse water quality conditions detected in the system for 2025 from the regular sampling schedule.

When an adverse incident occurs, staff go beyond legislated requirements for response and corrective action by thoroughly reviewing all operational, sampling practices, equipment, hygiene and lab processes.

MECP Drinking Water System Inspection Report

On July 3rd, 2025, both Town's distribution systems underwent a focused inspection by an MECP Drinking Water Inspector. The inspection covered the period from August 14, 2024, to June 30, 2025.

The inspection report identified zero non-compliance items and no recommendations of best practice; therefore, both systems received a **100% Inspection Rating**.

Regulatory Updates

Drinking Water Quality Management Standard

On April 22, 2025, the MECP provided a draft of the updated Drinking Water Quality Management Standard for review. These updates are intended to provide clarification, reflect current practice in municipal residential drinking water systems, and enable auditing of practices used to summarize monitoring data.

Underground Infrastructure Notification System Act

Ontario One Call (ON1Call) is responsible for administering the Ontario Underground Infrastructure Notification System Act, 2012. The Act designates ON1Call as the single point of contact in Ontario to request the location of underground infrastructure prior to digging.

Non-municipal owners and operators of underground infrastructure, as specified under the Act, were required to join ON1Call as of June 19, 2013. Municipalities were required to join ON1Call a year later, by June 19, 2014. The Town voluntarily joined as a member in June 2013. The update on this program can be found in **Section 8 – Monitoring and Improvement Initiatives**.

MECP Watermain Disinfection Procedure

All municipal operating authorities are required to use AWWA Standard C651 (Disinfecting Watermains) for addition, replacement or repair of pipes forming the distribution system, as a condition of Drinking Water Works Permits. In August 2020, the MECP working with the Ontario Water Works Association and municipal stakeholders finalized and implemented requirements of C651 and developed alternative procedures to be used during emergency repairs. The Town of Lincoln's current procedures for watermain break repair as well as commissioning new watermain already encompass the changes in this document.

Training and Competency

Operator training is required by law to maintain water licenses and ensure competency. In 2025, training records were reviewed for all licensed operators in an ongoing effort to ensure that staff remain competent and participate in training opportunities that are engaging and relevant to Town operations.

Operators and key water staff participated in several diverse course offerings in 2025 aimed at broadening their knowledge. This included training in safe drinking water act, cross connection backflow prevention, adverse drinking water, O. Reg 170, fire hydrant and valve operations, supplier specific training, watermain commissioning and many other topics.





5. Flow and Loss Data

Flow Data

Water consumed by the Town of Lincoln is measured by the Niagara Region and provided monthly to the Town. In 2025, a total of 2,747,702 cubic meters (m^3) of water flowed to the Town of Lincoln.

Beamsville

In 2025, the Region of Niagara supplied 1,623,592 m^3 to Beamsville.

Table 4 – Annual Totals

Year	Beamsville (m^3)
2006	1,422,652
2007	1,613,349
2008	1,437,779
2009	1,255,899
2010	1,348,464
2011	1,401,503
2012	1,384,166
2013	1,314,204
2014	1,367,702
2015	1,380,213
2016	1,462,331
2017	1,316,411
2018	1,359,226
2019	1,342,244
2020	1,484,710
2021	1,500,845
2022	1,464,744
2023	1,439,050
2024	1,562,494
2025	1,625,592

Jordan-Vineland


In 2024, the Region of Niagara supplied 1,033,353 m^3 to Jordan-Vineland.

Table 5 – Annual Totals

Year	Jordan-Vineland (m^3)
2006	1,099,607
2007	1,132,574
2008	859,546
2009	971,954
2010	870,980
2011	901,932
2012	954,016
2013	939,954
2014	871,400
2015	945,100
2016	990,541
2017	907,900
2018	972,359
2019	907,040
2020	1,039,124
2021	1,030,873
2022	1,074,423
2023	1,063,457
2024	1,033,353
2025	1,124,110


To review from a monthly perspective, **Figures 1 and 2** show the monthly consumptions for 2025 for both systems.

Figure 1 – Monthly Totals for 2025 - Beamsville

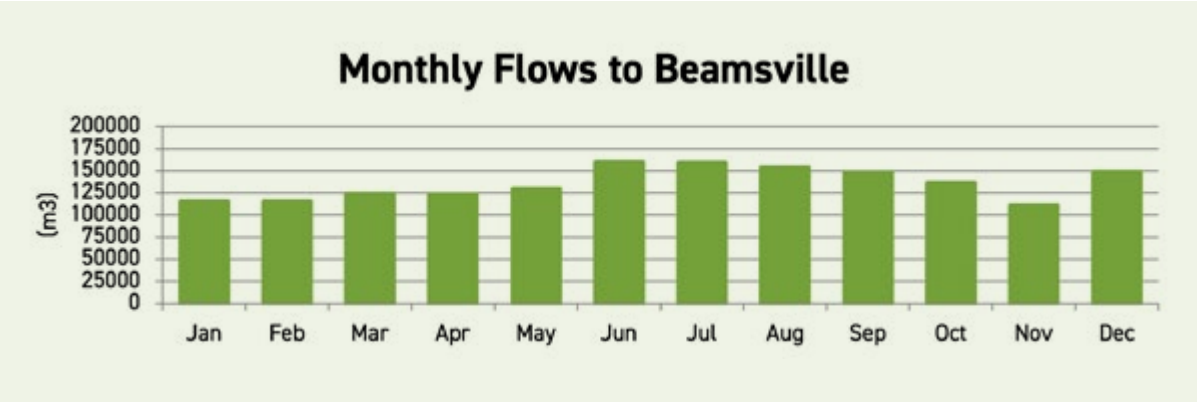

The average monthly consumption for Beamsville in 2025 was 135,299m³ a 3.9% increase from 2024. As expected, the highest consumption months occurred in the summer, likely due to hot weather influences on irrigation, evaporative cooling, recreational pools and landscaping requirements.

Figure 2 – Monthly Totals for 2025 – Jordan-Vineland

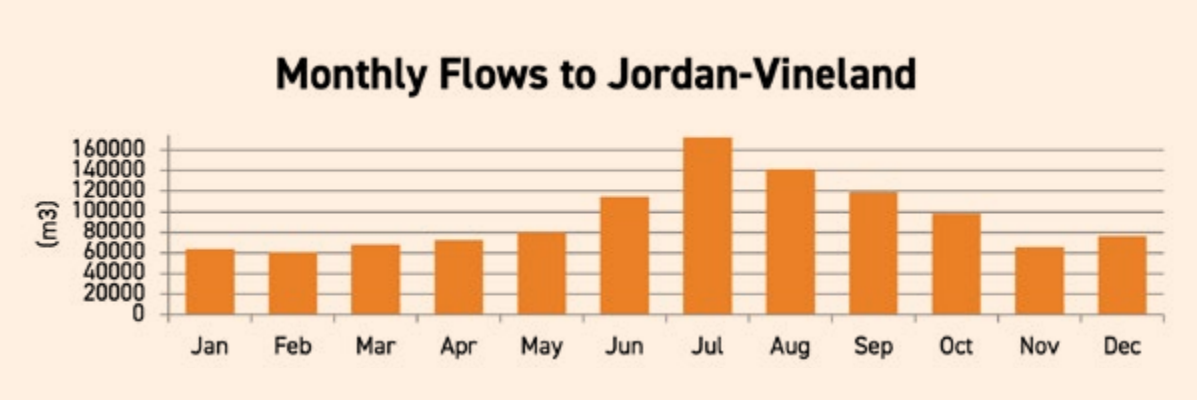

The average monthly consumption for Jordan-Vineland in 2025 was 93676m³ – a 8.7 % increase from 2024. As expected, the highest consumption months occurred in the summer, likely due to hot weather influences on irrigation, evaporative cooling, recreational pools and landscaping requirements.

All water demands were met in both systems; thus the Town was not required to implement the outdoor use restrictions under section 73 (b) of the Water Supply By-law No. 01-134.

The Town's Drinking Water License does not limit demand or flows to the Town, so a comparison to license limits is not required.

Beamsville

The 2025 average highest demand for Beamsville occurred in June, which aligns with the high monthly demands in the warmer summer months.

The Town of Lincoln's Memorandum of Understanding with Niagara Region for water servicing (2021) states that the objective of the Region of Niagara is to meet or exceed the projected demands from the most recent Master Servicing Plan. This objective appears to be satisfied for the Beamsville system.

Jordan-Vineland

The 2025 average highest demand for Jordan-Vineland occurred in July, which aligns with the high monthly demands in the warmer summer months.

The Town of Lincoln's Memorandum of Understanding with the Niagara Region for water servicing (2021) states that the objective of the Region of Niagara is to meet or exceed the projected demands from the most recent Master Servicing Plan. This objective appears to be satisfied for the Jordan-Vineland system.

Loss Data

Water loss is monitored together by the Finance department and the Waterworks department. Water loss is basically defined as per below:

Water Loss = Total Water Purchased − Non-revenue Water
(fire departments use, etc.)

Water loss for 2025 is estimated at **7.8%**. Unbilled water usage from fire training exercises, firefighting, watermain maintenance and main breaks is coarsely estimated and incorporated into this 2025 figure. The direct causes of the loss in both systems is not known without further investigation, testing and monitoring, but is typically attributed to such causes as:

- Unknown leaks (although leak detection monitoring is performed, not all mains can be tested in their entirety each year, and leak detection itself is complicated by traffic noise, normal industrial usage and ground conditions).
- System use from hydrants and main breaks (although estimates of losses are provided from regular maintenance flushing activities, fire department training/use and from main break events, there is room for significant error in these coarse estimates, which may account for some of the unaccounted loss).
- Usage through unknown or illegal connections.

Figure 3 – shows the water loss by year for both systems.

Figure 3 – Water Loss by Year (%), both systems combined.



The black trend line shows the overall trend of water loss since 2006 for both systems. In general, water loss by percentage has a decreasing trend.

The 2025 system losses are considered favourable as a water loss target within the industry, but the Town will continue to look at where further improvements can be made.



6. Infrastructure

Capital Projects and Purchases

The Town updated the 10-year capital plan to ensure that it represents the most current water distribution system improvement needs.

The following system-specific capital projects were carried out in 2025:

Beamsville

- Greenlane Phase 1A Watermain Replacement Design from Lincoln Avenue to Ontario Street.
- Lincoln Avenue Watermain Replacement Design from Meadowood Lane to the South Service Road.

Jordan-Vineland

- Greenlane Watermain Replacement from Victoria Avenue to west limit.
- Glen Elgin Booster Station Upgrades (pumps and associated piping).
- Prudhommes and Victoria Avenue Watermain Upgrades commenced.

Rehabilitation and Repairs

Watermain

A total of 12 watermain breaks occurred in both water systems during 2025:

- 8 watermain breaks occurred in the Beamsville system.
- 4 watermain break occurred in the Jordan-Vineland system.

Table 6 shows the watermain break summary.
Figure 4 shows the overall downward trend for the total number of watermain breaks.

Table 6 – 2025 Watermain Break Summary

Date	Location	Type of Pipe	Suspected Cause	Replacement in 10-year Capital Plan
January	Greenlane and Juniper	Cast	Age	2025
January	Laurie Avenue	Cast	Age	TBD
January	3383 Tallman	Cast Iron	Age	2030
February	4748 Ontario Street	PVC	Age	TBD
February	4748 Ontario Street	PVC	Repair Clamp Failure	TBD
February	4646 Lincoln Avenue	Cast	Age	2025
March	4914 Union Road	PVC	Stress	Monitor
March	Lincoln Ave/South Service	Cast/PVC	Construction	2025
April	Lincoln Ave/Greenlane	Cast	Age	2025
July	Lincoln Avenue	Cast	Age	2025
November	3345 Tallman Drive	Cast	Age	2030
November	4430 Jordan Road	AC	Construction	2026/2027

The number of breaks is generally less than the numbers experienced in the early 2000s. This is due to the aggressive replacement and rehabilitation program that has been in place. However, the following should be noted:

- Other metallic piping requiring attention still remains, such as factory cement lined ductile iron and cast iron piping that was later cement lined to improve water quality. All of the remaining metallic pipe is expected to require replacement within the next 5 to 20 years. This variation in expected lifespan makes scheduling of replacement challenging, but age and performance will continue to be criteria considered as part of the Town's Asset Management Plan each year when reviewing the watermain needs in the 10-year Capital Plan.

Figure 4 – Town of Lincoln - Watermain Breaks (Beamsville and Jordan-Vineland)

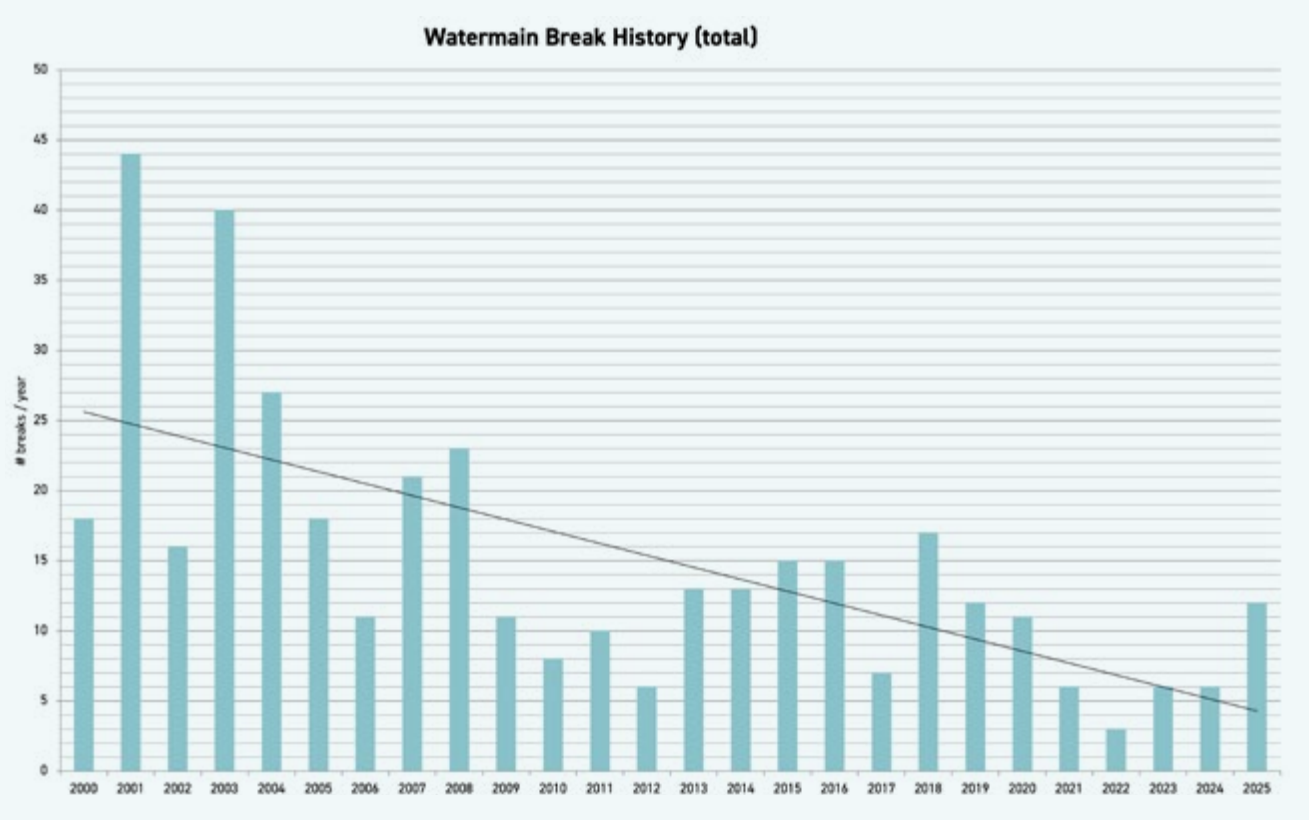


Figure 5 shows the overall downward trend for the total remaining amounts of metallic piping still in service in both water systems. The Town has been very progressive and successful in removing all non-cement lined cast iron piping from both water distribution systems.

2025 saw an increase in breaks due to the colder winter weather and freeze and thaw cycles.


2 breaks were due to construction.







Figure 5 – Remaining Metallic Pipe

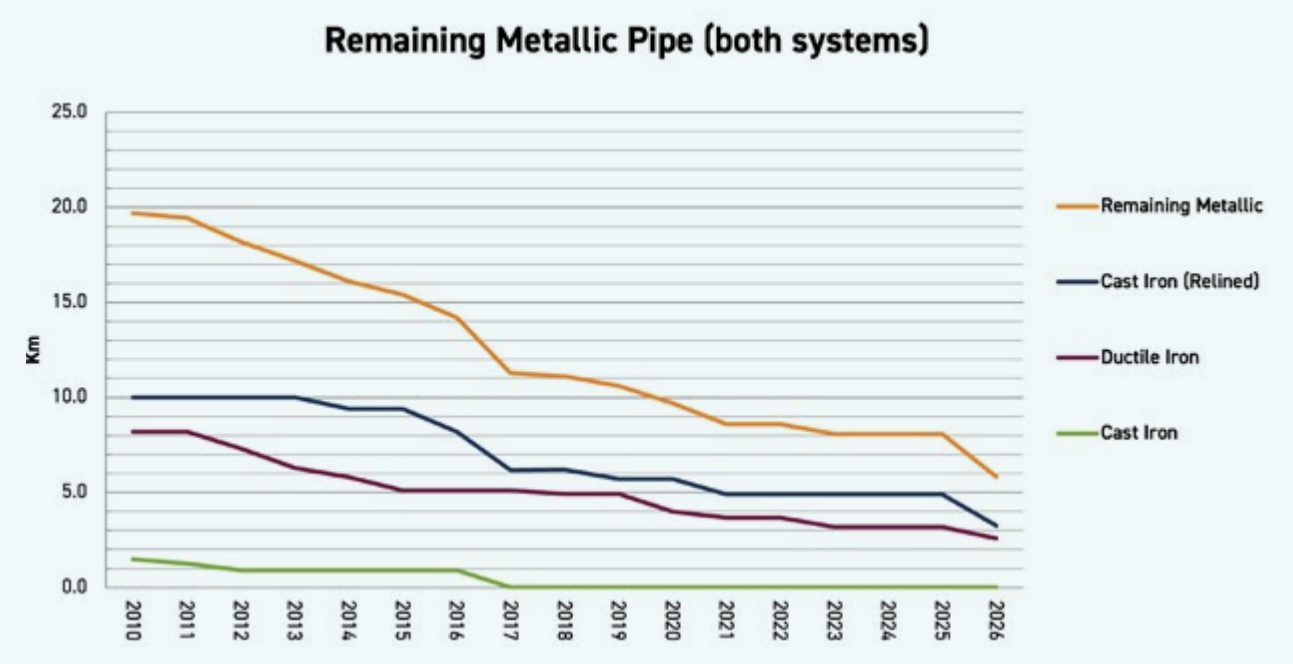

Frozen Water Services

During the winter of 2025 the Town Water Department responded to zero frozen water service calls.

Should a significant cold winter occur, the Town was prepared to handle frozen water services as per the following initiatives:

- Identified the risks associated with frozen water services in the drinking water system Risk Assessment controlled under the Drinking Water Quality Management System.
- Lowered and insulated the known services considered vulnerable to freezing due to their shallow depth.
- This Drinking Water Quality Management System includes a standard operating procedure which addresses the steps involved in thawing water services and detailed directions for hooking up temporary water supply between homes.

Booster Pumping Stations

Regular maintenance and repairs were completed at all three booster stations in both systems. The Town continues to work closely with the Region of Niagara to maintain close communication about pressure or supply interruptions related to pumping stations.

In 2025 the Glen Elgin Booster Pumping Station pumps and motor were rebuilt and replaced cast pipes with stainless steel pipes, chamber was waterproofed.

Table 7 shows the metrics for specific operation and maintenance tasks completed by staff in 2025. This will be a baseline year to compare to going forward.

Table 7 – 2025 Performance Metrics

Action	Number Completed
Hydrants Flushed	1025
Valves Exercised	200
Locates Completed	1801
Samples Collected	2027
Work orders Completed	782
Complaints Resolved	3
Hydrants Flow Tested and Color Coded	4
Chambers Inspected	16

7. Region of Niagara - Supply

Master Servicing Plan

The Region of Niagara's Master Servicing Plan (MSP) remains a key guiding document for infrastructure planning. Niagara Region is preparing to initiate an update to the Water and Wastewater MSP, which will incorporate the 2051 growth forecast and a full build-out scenario to support long-term servicing and infrastructure needs across the region. The update commenced in 2025 and is planned to continue through 2026.

Capital Infrastructure Projects

Greenlane Transmission Water Supply Main Replacement from Ontario Street to Lincoln Avenue.

DWQMS/Compliance Working Group

The Region of Niagara hosts a quarterly meeting with the 12 local area municipality DWQMS Representatives and Public Health to discuss emerging regulatory and QMS changes and updates. This is a great forum for benchmarking with other municipalities as well as generating discussion on areas of improvement to the DWQMS.

Memorandums of Understanding

As a result of discussions with several local municipalities and the Regional Municipality of Niagara, the Region updated the Memorandums of Understanding (MOUs) between the Region, as supplier of treated drinking water, and each local municipality, as receiver of the drinking water. The previous MOU was created in 2006 and needed to include more quality and system scope details related to both parties. The MOU was developed by a working group representing the 12 local municipalities and the Region. The updated MOUs were approved by the Region and local municipalities in the summer of 2016. The MOU is a critical document that is relied upon in the Drinking Water Quality Management System, as it defines the scope, quality and service requirements for the drinking water received into the Town systems.

8. Monitoring and Improvement Initiatives

In 2025, staff continued to place an increased emphasis on proactive measures to ensure the Town's ability to efficiently deliver safe drinking water.

Backflow Prevention

Backflow is a term for an unwanted flow of water in the reverse direction that can be a serious health risk for the contamination of potable water supplies with foul water. The Town of Lincoln recognizes a need to address the risk of backflow into its drinking water systems from privately owned properties. This is being achieved through the Backflow Prevention Program, as set out under Town of Lincoln By-Law #07-63 (as amended).

The main components of the program involve:

- *A survey of the property to identify cross-connections, risks and the recommended type of backflow prevention device required,*
- *Installation of the required backflow prevention device, where needed, under a Town of Lincoln plumbing permit, and*
- *Maintenance and annual testing of the backflow prevention device.*

In 2025 the testing compliance was 77.9%, a slight increase from 2024. More installations have occurred.

Monitoring Program for Lower Residual Areas

The objective of this ongoing project is to increase awareness of system monitoring needs, and to ensure consistent quality of water throughout the water distribution systems. Staff enhanced the 'dead end' water quality study by continuing to test the water in areas where free chlorine residual may decrease below critical control limits and perform hydrant flushing to refresh the water, as per the Town's risk assessment.

Factors that may reduce chlorine residual include infrastructure 'dead ends', low water demand, excessively large main, elevated temperatures and combinations of these factors.

The Town has a total of 9 auto flushers.

- 1 at 4696 King Street
- 1 at 4607 King Street
- 1 on Martin Road South,
- 1 at Martin Road North
- 1 at 3500 South Service Road
- 1 on Bartlett Road
- 1 on George Street
- 1 on Aberdeen Road
- 1 on Greenlane Road

Staff continually tested, monitored and optimized the operation of these units which has eliminated the need to regularly flush this dead end results in a reduction of water loss from flushing.

Sensitive areas continue to be tested under an overall plan to further establish flushing frequencies and develop solutions.

Focused Water Quality Monitoring

In both systems, staff continue to trend water for key quality indicators including chlorine residuals, trihalomethanes, lead, pH, alkalinity, main breaks, and flows.

Reactive measures are necessary to address adverse water quality conditions as they occur; however, the best system management practices are based on proactive measures that prevent them from occurring.

Smart Hydrant Technology and Leak Detection

The leak detection program was continued in 2025.

The Town has 12 Smart Hydrants which are actively monitoring pressures, temperatures and completing leak detection within 500m of each devise. These hydrant inserts are able to be relocated when needed and are currently strategically placed across Town. Over the next 10 years, staff would like to expand on the Smart Hydrant insert program to improve monitoring and to enhance our understanding of pressures and temperatures within the system.


Water Meter Program

In 2021 the Town completed the Town Wide meter replacement program upgrading to Advance Metering Infrastructure (AMI) smart technology. As part of the program the Town also launched a customer service portal which will allow users to have real time usage information.

Ontario One-Call

On June 4, 2013 the Town of Lincoln officially started its membership with Ontario One Call. Since that time, requests for locates have increased significantly. As a result, adjustments have been made in the operating budget to account for the increased staff time spent on providing locates (annual totals shown in **Figure 7**). The Town will continue to monitor the overall locate request trends and related impacts on our operational resources

Figure 7 – Total Number of Locates per Year (metrics)

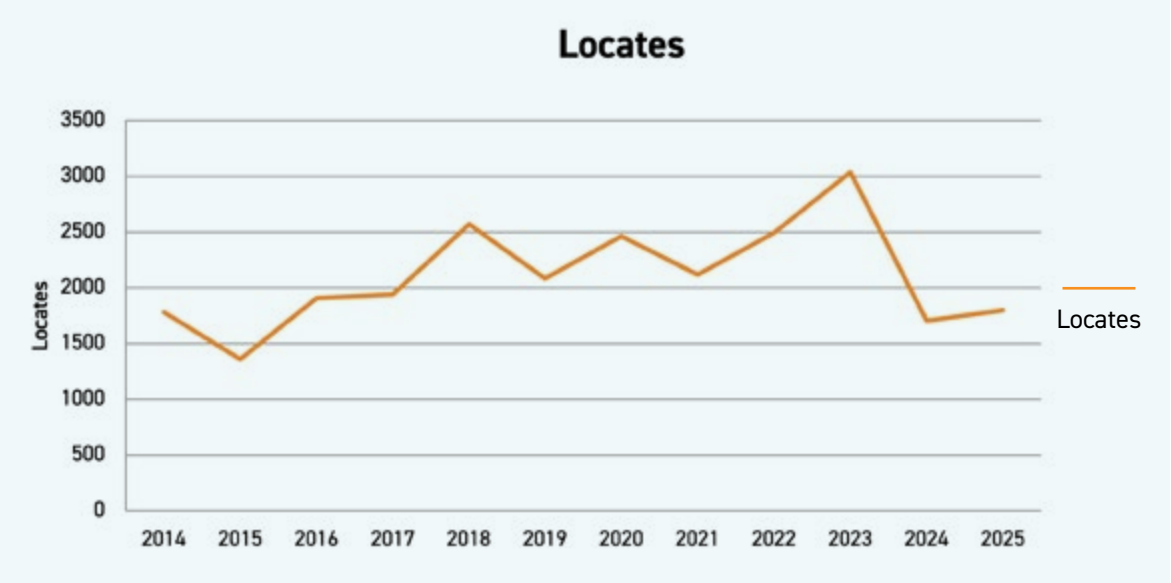

The Town uses (UtiLocate) in order to help streamline the locate process. This software system allows for the instant download and assignment of locate requirements for water operators in the field. The water operator then directly submits the digital locate reports to the requestor. This new software system has greatly improved operational efficiencies by reducing the burden imposed on Town staff in processing the increased work order requests and improved customer service turnaround times for providing private locates.

9. Staffing

The Town waterworks department currently has a complement of a Manager of Operations, a Supervisor of Environmental Services and seven (7) Water Maintenance Operators.

- The seven Water Maintenance Operators consist of five with a Class 3 license and two with a Class 2 license.
- The Supervisor, Environmental Services held a Class 3 license.

The waterworks department is also heavily supported by our Regulatory Compliance Team.

License Renewals

There was one Drinking Water Operator license due for renewal in 2025.

License Upgrades

There were two Drinking Water Operator license upgrades in 2025. All operators now hold a Class 3 license.

The MECP issues licenses for water distribution system operators, which are required by law to operate the system. Licenses must be renewed every three years and eligibility for renewal is based on meeting the requirements for training and operational hours.

Operator-In-Charge Designation

Under Ontario Regulation 128/04, the owner of a drinking water system shall designate one or more operators as operators-in-charge (OIC), with specific responsibilities prescribed in the regulation. During normal operations, all water operations staff complete key OIC related tasks as described under O.Reg 218/04.

- Pressure Reducing Valve (PRV) chamber maintenance and optimization.
- Hydrant Flow Testing and color coding.
- Leak Detection.
- New Watermain Commissioning.
- Locate templating.



10. Municipal Drinking Water Licensing Program

The Municipal Drinking Water Licensing Program is a five-stage initiative by the MECP under the Safe Drinking Water Act, 2002. **The Town of Lincoln maintains its Certificate of Accreditation as an Operating Authority for its water distribution systems, and both system licenses and permits are in place.** Table 8 lists the status of the key elements for water licensing.

Table 8 – Municipal Drinking Water Licensing Program Progress

Stage	Status
License	Renewed January 21, 2025.
Permit	Renewed January 21, 2025.
Operational Plan	Operation plan was re-endorsed on July 29, 2024.
Accreditation	This accreditation process is required every three years and the new certificate expires January 10, 2028. (See appendix C).
Financial Plan	Updated Rate Study was completed in Q3 2024 and council approved the updated rates in January 2024.





11. Quality Management System

The Quality Management System (QMS) is fully integrated into waterworks operations and is maturing and improving with time. Council should remain aware of its commitments in the QMS Policy, which is the framework upon which to set the QMS.



In addition, Council must be fully aware of the Operational Plan and its principles. The Operational Plan is the overall guide to the QMS, like a road map to the system that describes how the Water Department performs all the activities described in this summary report. Many of the items covered in this report are managed under QMS processes and are monitored and improved upon based on initiatives in the QMS.

The current Operational Plan that was re-endorsed by Council in July 2024 is available through the Public Works library, or in the Public Works directory on the network.

Infrastructure Review

Infrastructure review is a required component of the DWQMS, where infrastructure includes piping and related infrastructure, but also buildings, workspace, process equipment, hardware, software, and supporting services such as transport or communication. The purpose of the review was to assess the adequacy of the infrastructure necessary to operate and maintain the water system.

On September 9, 2025, the Director of Public Works, Manager of Operations, Supervisor of Environmental Services and the Manager, Regulatory Compliance completed the annual review of infrastructure needs, in accordance with the Town's Operational Plan. Recommendations were translated accordingly into the 2025 waterworks operational and capital budgets and 10-year Capital Plan updates.

Management Review

Management review is a required component of the DWQMS. On September 9, 2025, the Director of Public Works, Manager of Operations, Supervisor of Environmental Services and the Manager, Regulatory Compliance completed the annual review in accordance with the Town's Operational Plan. Management review focuses on the quality management system as a whole, and high-level operational topics. The review covered September 6, 2024 to September 9, 2025 and provided a review of the key indicators of the QMS performance. Deficiencies, decisions and action items are summarized in **Table 9** below.

Table 9 – Management Review Communication

Topic	Deficiency / Status	Decision / Action Item
Incidents of Regulatory Non-Compliance	There are no incidents of regulatory non-compliance.	NONE
Deviations from Critical Control Points	Reviewed deviations: • CCP1 – Improper break repair: none. • CCP2 – New connections: none. Some new high-risk private commissioning required before connections, to reduce risk. Going well. • CCP3 – Design: None • No concerns with deviation or response for any of the CCPs.	NONE
Internal Audits	Third party audit occurred on October 15, 2025, by SAI Global. Effective overall management system. No major non-conformances or minor non-conformances and no OFI's. Internal audit completed in June 24, 2025 by contracted service – Acclaims. Internal audit results were reviewed by going over corrective and preventative actions. All OFI's have been documented and have been addressed through the corrective and preventative actions database.	NONE

Topic	Deficiency / Status	Decision / Action Item
Changes that Could Affect QMS	HAA sampling was implemented in 2017, budget increase needed. Potential level 3 distribution system class in the future with growth. (I.e., Extra 7 hours a year for training per staff member when operators have level 3 license, higher demand on staff for # of samples and extra infrastructure to maintain).	NONE
Operational Plan	The Town's Operational Plan was re-endorsed on July 29, 2024.	No action recommended
Suitability, adequacy, effectiveness	Suitability: With continued maturing, QMS remains suited to use at the Town. Effectiveness: As per indicators above, QMS appears to be 'working', helping with MECP inspections, trending, overall review, record-keeping and day to day operations etc. Adequacy: Needs being incorporated into Town's budget process. As such, no recommended changes at this time.	No action recommended



12. Spotlight on 2026

Capital Projects

- Vine Haven Booster Pump Station – system rehabilitation

Water Quality

Staff expects to continue a number of projects and purchases with respect to improving distribution system function and efficiency, highlighted in Section 6.

- Water quality trending and analysis will remain a focus in 2026 and the e.RIS data management system has been fully implemented.
- Continue improving backflow program.

DWQMS

- In accordance with section 21 of the Safe Drinking Water Act, 2002, the Minister approved version 3 of the Drinking Water Quality Management Standard on February 2026. These updates provide clarification, reflect current practice in municipal residential drinking water systems and enable auditing of practices used to summarize monitoring data.
- Under Element 21 (Continual Improvement) of the Drinking Water Quality Management Standard new Best Management Practices were released on October 2025. The Town has already begun implementing changes to their procedures.
- Continue to develop GIS system.

Staffing

- Continue to support Operator training opportunities as per O. Reg 128/04.

Asset Management Plan

- Updating ArcGIS to include all Town assets and digitize QMS forms for increasing operational efficiencies for Water Operators and the Town.

Growth & Looking Forward

- The Lincoln Water Distribution systems are anticipated to potentially trigger an MECP system classification upgrade from Class 2 to Class 3 in the future resulting from expected development growth.
    - > Additional watermain added to both systems projected to be 10km (along with the associated additional hydrants, valves and meters).
    - > Staff have initiated conversations with the MECP to complete a revised assessment of the Town's systems classification. An update will be provided when the assessment is complete.
- Staff would like to make Council aware that moving forward the need for additional operational staff resources related to growth will be further monitored and assessed in detail on an ongoing basis.





Appendix A

Beamsville Water Distribution System

MECP Annual Report



Ontario **Drinking-Water Systems Regulation O. Reg. 170/03**

OPTIONAL ANNUAL REPORT TEMPLATE

Drinking-Water System Number:	**260004319**
Drinking-Water System Name:	**Beamsville Distribution System**
Drinking-Water System Owner:	**The Corporation of the Town of Lincoln**
Drinking-Water System Category:	**Large Municipal Residential**
Period being reported:	**January 1, 2025, to December 31, 2025**

Complete if your Category is Large Municipal Residential or Small Municipal Residential	***Complete for all other Categories.***
Does your Drinking-Water System serve more than 10,000 people? Yes [X] No [ ] **Is your annual report available to the public at no charge on a web site on the Internet? Yes [X] No [ ]** **Location where Summary Report required under O. Reg. 170/03 Schedule 22 will be available for inspection.** Municipal Offices 4800 South Service Road Beamsville, ON L3J 1L3 Website: www.lincoln.ca	**Number of Designated Facilities served:** **Did you provide a copy of your annual report to all Designated Facilities you serve?** **Yes [ ] No [ ]** **Number of Interested Authorities you report to:** **Did you provide a copy of your annual report to all Interested Authorities you report to for each Designated Facility?** **Yes [ ] No [ ]**

Note: For the following tables below, additional rows or columns may be added, or an appendix may be attached to the report

List all Drinking-Water Systems (if any), which receive all of their drinking water from your system:

Drinking Water System Name	Drinking Water System Number
None	

Did you provide a copy of your annual report to all Drinking-Water System owners that are connected to you and to whom you provide all of its drinking water?
Yes [X] No [ ]

Indicate how you notified system users that your annual report is available, and is free of charge.

- **[X] Public access/notice via the web**
- **[ ] Public access/notice via Government Office**
- **[ ] Public access/notice via a newspaper**
- **[X] Public access/notice via Public Request**
- **[ ] Public access/notice via a Public Library**
- **[ ] Public access/notice via other method** _____

Describe your Drinking-Water System

The Town of Lincoln owns and operates the Beamsville Distribution System. The system receives its supply of treated water from the Niagara Region Grimsby Water Treatment Facility via a transmission main. Water is re-chlorinated at the Region's booster pumping station, west of the Town border. Water is also re-chlorinated at the Hixon Street storage reservoir, owned and operated by the Region of Niagara. Both the booster station and the storage reservoir directly serve the Town of Lincoln distribution system.

The Beamsville Distribution System is comprised of approximately 65km of watermain.

The system contains 456 hydrants, 17 pressure reducing valve chambers and one Town-owned and operated pressure booster pumping station equipped with a standby diesel generator.

No re-chlorination is performed by the Town of Lincoln within the Beamsville Distribution System.

List all water treatment chemicals used over this reporting period

Not Applicable

Were any significant expenses incurred to?

- **[ ]** Install required equipment
- **[X]** Repair required equipment
- **[X]** Replace required equipment

Please provide a brief description and a breakdown of monetary expenses incurred

Approximately $67,236 for operational repairs (including water main maintenance, breaks repairs, frozen water service restoration, hydrant repairs and pressure booster pumping station repairs) and approximately $ 2,552,424 for capital replacement (including construction, inspection and material testing for watermain replacement projects).

Provide details on the notices submitted in accordance with subsection 18(1) of the Safe Drinking-Water Act or section 16-4 of Schedule 16 of O.Reg.170/03 and reported to Spills Action Centre

Incident Date	Parameter	Result	Unit of Measure	Corrective Action	Corrective Action Date

Microbiological testing done under the Schedule 10, 11 or 12 of Regulation 170/03, during this reporting period.

	Number of Samples	Range of E.Coli Or Fecal Results (min #)-(max #)	Range of Total Coliform Results (min #)-(max #)	Number of HPC Samples	Range of HPC Results (min #)-(max #)
Raw					
Treated					
Distribution	520	0-0	0-0	520	0-7

Operational testing done under Schedule 7, 8 or 9 of Regulation 170/03 during the period covered by this Annual Report.

	Number of Grab Samples	Range of Results (min #)-(max #)	Unit of Measure
Turbidity			
Chlorine (free)	609	0.63-1.55	mg/L
Fluoride (If the DWS provides fluoridation)			

***NOTE**: For continuous monitors use 8760 as the number of samples.*

Summary of additional testing and sampling carried out in accordance with the requirement of an approval, order or other legal instrument.

Date of legal instrument issued	Parameter	Date Sampled	Result	Unit of Measure

Summary of Inorganic parameters tested during this reporting period or the most recent sample results

Parameter	Sample Date	Result Value	Unit of Measure	Exceedance
Antimony				
Arsenic				
Barium				
Boron				
Cadmium				

Chromium				
***Lead**				
Mercury				
Selenium				
Sodium				
Uranium				
Fluoride				
Nitrite				
Nitrate				

*only for drinking water systems testing under Schedule 15.2; this includes large municipal non-residential systems, small municipal non-residential systems, non-municipal seasonal residential systems, large non-municipal non-residential systems, and small non-municipal non-residential systems

Summary of lead testing under Schedule 15.1 during this reporting period

(applicable to the following drinking water systems; large municipal residential systems**,** small municipal residential systems, and non-municipal year-round residential systems)

Location Type	Number of Samples	Range of Lead Results (min#) – (max #)	Unit of Measure	Number of Exceedances
Plumbing	**-**	**-**	**-**	**-**
Distribution	8	<0.00002 -0.00045	mg/L	0

Summary of Organic parameters sampled during this reporting period or the most recent sample results


Parameter	Sample Date	Result Value	Unit of Measure	Exceedance
Alachlor				
Aldicarb				
Aldrin + Dieldrin				
Atrazine + N-dealkylated metobolites				
Azinphos-methyl				
Bendiocarb				
Benzene				
Benzo(a)pyrene				
Bromoxynil				
Carbaryl				
Carbofuran				
Carbon Tetrachloride				
Chlordane (Total)				
Chlorpyrifos				
Cyanazine				
Diazinon				
Dicamba				
1,2-Dichlorobenzene				
1,4-Dichlorobenzene				

Dichlorodiphenyltrichloroethane (DDT) + metabolites				
1,2-Dichloroethane				
1,1-Dichloroethylene (vinylidene chloride)				
Dichloromethane				
2-4 Dichlorophenol				
2,4-Dichlorophenoxy acetic acid (2,4-D)				
Diclofop-methyl				
Dimethoate				
Dinoseb				
Diquat				
Diuron				
Glyphosate				
Heptachlor + Heptachlor Epoxide				
Lindane (Total)				
Malathion				
Methoxychlor				
Metolachlor				
Metribuzin				
Monochlorobenzene				
Paraquat				
Parathion				
Pentachlorophenol				
Phorate				
Picloram				
Polychlorinated Biphenyls(PCB)				
Prometryne				
Simazine				
HAA (NOTE: show latest annual average)				
THM (NOTE: show latest annual average)	Q1 = Feb 18 Q2 = May 13 Q3 = Aug 19 Q4 = Nov 19	**22.52**	ug/L	None
Temephos				
Terbufos				
Tetrachloroethylene				
2,3,4,6-Tetrachlorophenol				
Triallate				
Trichloroethylene				
2,4,6-Trichlorophenol				
2,4,5-Trichlorophenoxy acetic acid (2,4,5-T)				
Trifluralin				
Vinyl Chloride				

List any Inorganic or Organic parameter(s) that exceeded half the standard prescribed in Schedule 2 of Ontario Drinking Water Quality Standards.

Parameter	Result Value	Unit of Measure	Date of Sample
N/A			



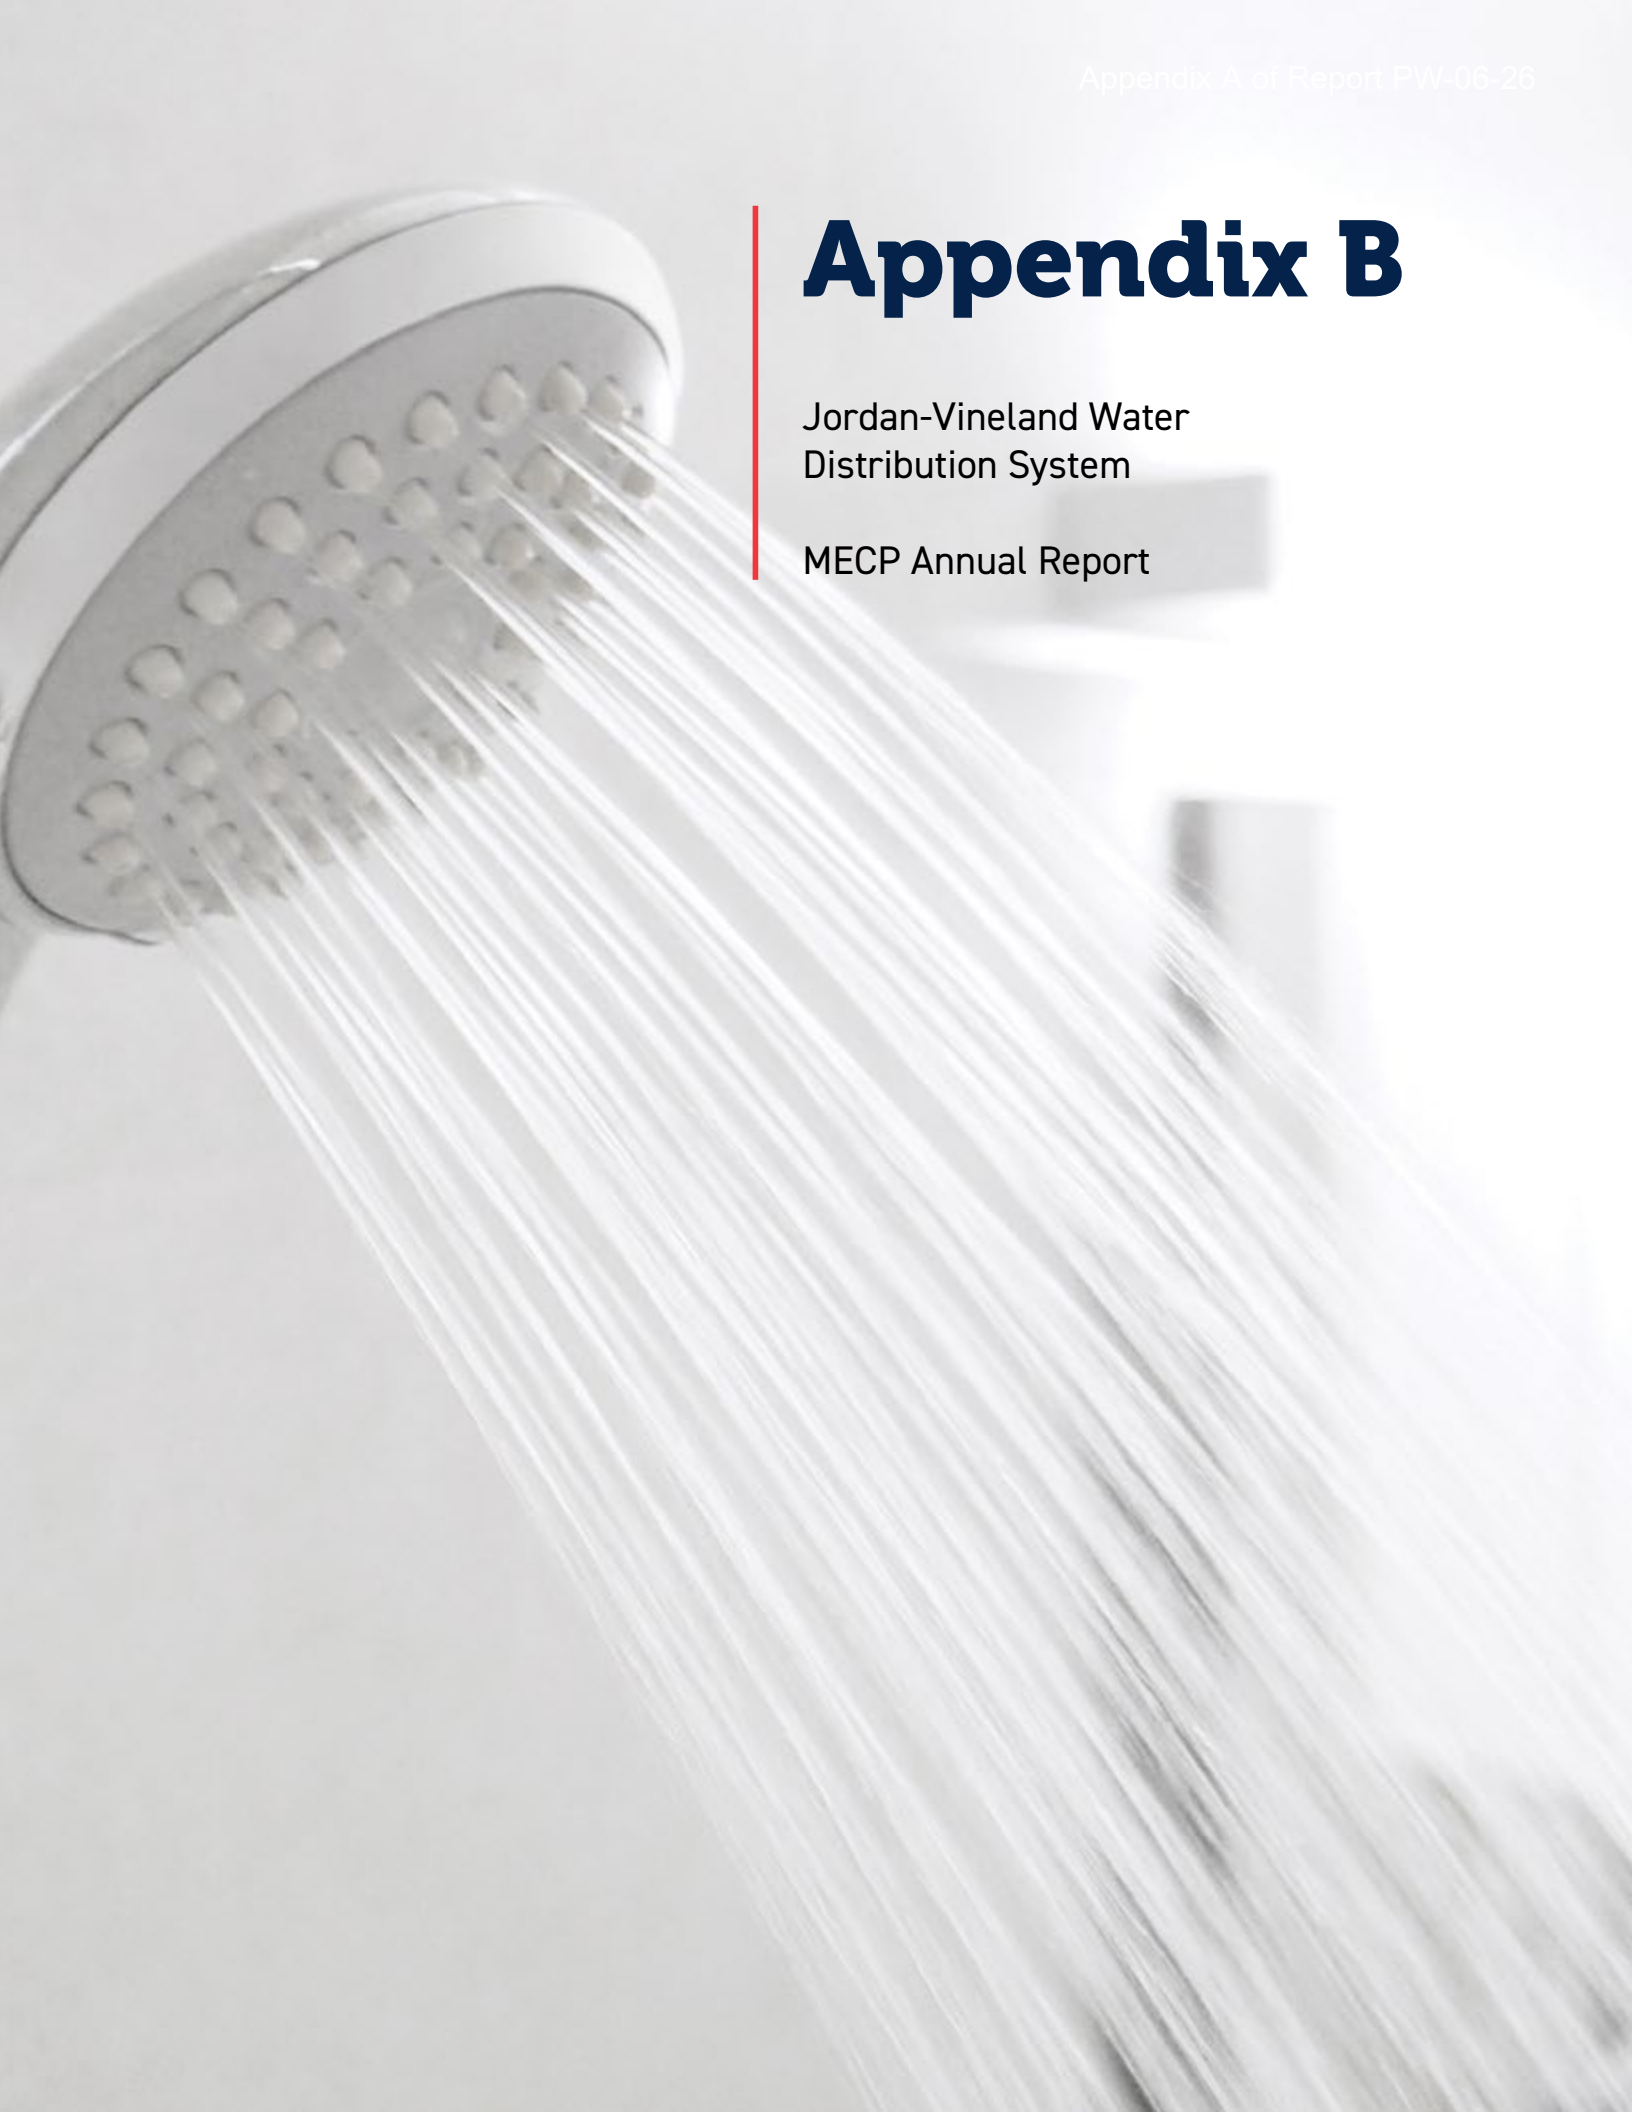

Appendix B

Jordan-Vineland Water Distribution System

MECP Annual Report

OPTIONAL ANNUAL REPORT TEMPLATE

Drinking-Water System Number:	**260004306**
Drinking-Water System Name:	**Jordan-Vineland Distribution System**
Drinking-Water System Owner:	**The Corporation of the Town of Lincoln**
Drinking-Water System Category:	**Large Municipal Residential**
Period being reported:	**January 1, 2025, to December 31, 2025**

Complete if your Category is Large Municipal Residential or Small Municipal Residential

Does your Drinking-Water System serve more than 10,000 people? Yes [ ] No [X]

Is your annual report available to the public at no charge on a web site on the Internet? Yes [X] No [ ]

Location where Summary Report required under O. Reg. 170/03 Schedule 22 will be available for inspection.

Municipal Offices
4800 South Service Road
Beamsville, ON L3J 1L3

Website: www.lincoln.ca

Complete for all other Categories.

Number of Designated Facilities served:

Did you provide a copy of your annual report to all Designated Facilities you serve?
Yes [ ] No [ ]

Number of Interested Authorities you report to:

Did you provide a copy of your annual report to all Interested Authorities you report to for each Designated Facility?
Yes [ ] No [ ]

Note: For the following tables below, additional rows or columns may be added, or an appendix may be attached to the report

List all Drinking-Water Systems (if any), which receive all of their drinking water from your system:

Drinking Water System Name	Drinking Water System Number
None	

Did you provide a copy of your annual report to all Drinking-Water System owners that are connected to you and to whom you provide all of its drinking water?
Yes [X] No [ ]

Indicate how you notified system users that your annual report is available, and is free of charge.

- **[X] Public access/notice via the web**
- **[ ] Public access/notice via Government Office**
- **[ ] Public access/notice via a newspaper**
- **[X] Public access/notice via Public Request**
- **[ ] Public access/notice via a Public Library**
- **[ ] Public access/notice via other method** _____

Describe your Drinking-Water System

The Town of Lincoln owns and operates the Jordan-Vineland Distribution System. The system receives its supply of treated water from the Niagara Region Decew Water Treatment Facility via a transmission main. Water is re-chlorinated at the Region's booster pumping station, located at the easterly limit of the Town. Water is also re-chlorinated at the Fifth Avenue Reservoir, which is owned and operated by the Region of Niagara. Both the booster station and the storage reservoir directly serve the Town of Lincoln distribution system.

The Jordan-Vineland Distribution System is comprised of approximately 42km of watermain.

The system contains 256 hydrants, two pressure reducing valve chamber and two Town-owned and operated pressure booster pumping stations.

No re-chlorination is performed by the Town of Lincoln within the Jordan-Vineland Distribution Systems.

List all water treatment chemicals used over this reporting period

Not applicable.

Were any significant expenses incurred to?

- **[ ]** Install required equipment
- **[X]** Repair required equipment
- **[X]** Replace required equipment

Please provide a brief description and a breakdown of monetary expenses incurred

Approximately $67,236 for operational repairs (including water main maintenance, breaks repairs, hydrant repairs and pressure booster pumping station repairs) and approximately $9,836,871 for capital replacement (including construction, inspection and materials testing for watermain replacement projects).

Provide details on the notices submitted in accordance with subsection 18(1) of the Safe Drinking-Water Act or section 16-4 of Schedule 16 of O.Reg.170/03 and reported to Spills Action Centre

Incident Date	Parameter	Result	Unit of Measure	Corrective Action	Corrective Action Date

Microbiological testing done under the Schedule 10, 11 or 12 of Regulation 170/03, during this reporting period.

	Number of Samples	Range of E.Coli Or Fecal Results (min #)-(max #)	Range of Total Coliform Results (min #)-(max #)	Number of HPC Samples	Range of HPC Results (min #)-(max #)
Raw					
Treated					
Distribution	416	0-0	0-0	416	0-6

Operational testing done under Schedule 7, 8 or 9 of Regulation 170/03 during the period covered by this Annual Report.

	Number of Grab Samples	Range of Results (min #)-(max #)	Unit of Measure
Turbidity			
Chlorine (free)	477	0.45-1.63	mg/l
Fluoride (If the DWS provides fluoridation)			

***NOTE**: For continuous monitors use 8760 as the number of samples.*

Summary of additional testing and sampling carried out in accordance with the requirement of an approval, order or other legal instrument.

Date of legal instrument issued	Parameter	Date Sampled	Result	Unit of Measure

Summary of Inorganic parameters tested during this reporting period or the most recent sample results

Parameter	Sample Date	Result Value	Unit of Measure	Exceedance
Antimony				
Arsenic				
Barium				
Boron				
Cadmium				
Chromium				
***Lead**				
Mercury				

Selenium				
Sodium				
Uranium				
Fluoride				
Nitrite				
Nitrate				

*only for drinking water systems testing under Schedule 15.2; this includes large municipal non-residential systems, small municipal non-residential systems, non-municipal seasonal residential systems, large non-municipal non-residential systems, and small non-municipal non-residential systems

Summary of lead testing under Schedule 15.1 during this reporting period
(applicable to the following drinking water systems; large municipal residential systems**,** small municipal residential systems, and non-municipal year-round residential systems)

Location Type	Number of Samples	Range of Lead Results (min#) – (max #)	Unit of Measure	Number of Exceedances
Plumbing	-	**-**	**-**	**-**
Distribution	8	0.00003 - 0.00069	mg/L	0


Summary of Organic parameters sampled during this reporting period or the most recent sample results

Parameter	Sample Date	Result Value	Unit of Measure	Exceedance
Alachlor				
Aldicarb				
Aldrin + Dieldrin				
Atrazine + N-dealkylated metobolites				
Azinphos-methyl				
Bendiocarb				
Benzene				
Benzo(a)pyrene				
Bromoxynil				
Carbaryl				
Carbofuran				
Carbon Tetrachloride				
Chlordane (Total)				
Chlorpyrifos				
Cyanazine				
Diazinon				
Dicamba				
1,2-Dichlorobenzene				
1,4-Dichlorobenzene				
Dichlorodiphenyltrichloroethane (DDT) + metabolites				
1,2-Dichloroethane				

1,1-Dichloroethylene (vinylidene chloride)				
Dichloromethane				
2-4 Dichlorophenol				
2,4-Dichlorophenoxy acetic acid (2,4-D)				
Diclofop-methyl				
Dimethoate				
Dinoseb				
Diquat				
Diuron				
Glyphosate				
Heptachlor + Heptachlor Epoxide				
Lindane (Total)				
Malathion				
Methoxychlor				
Metolachlor				
Metribuzin				
Monochlorobenzene				
Paraquat				
Parathion				
Pentachlorophenol				
Phorate				
Picloram				
Polychlorinated Biphenyls(PCB)				
Prometryne				
Simazine				
HAA (NOTE: show latest annual average)				
THM (NOTE: show latest annual average)	Q1 = Feb 18 Q2 = May 13 Q3 = Aug 19 Q4 = Nov 19	**40.2**	ug/L	None
Temephos				
Terbufos				
Tetrachloroethylene				
2,3,4,6-Tetrachlorophenol				
Triallate				
Trichloroethylene				
2,4,6-Trichlorophenol				
2,4,5-Trichlorophenoxy acetic acid (2,4,5-T)				
Trifluralin				
Vinyl Chloride				

List any Inorganic or Organic parameter(s) that exceeded half the standard prescribed in Schedule 2 of Ontario Drinking Water Quality Standards.

Parameter	Result Value	Unit of Measure	Date of Sample
N/A			

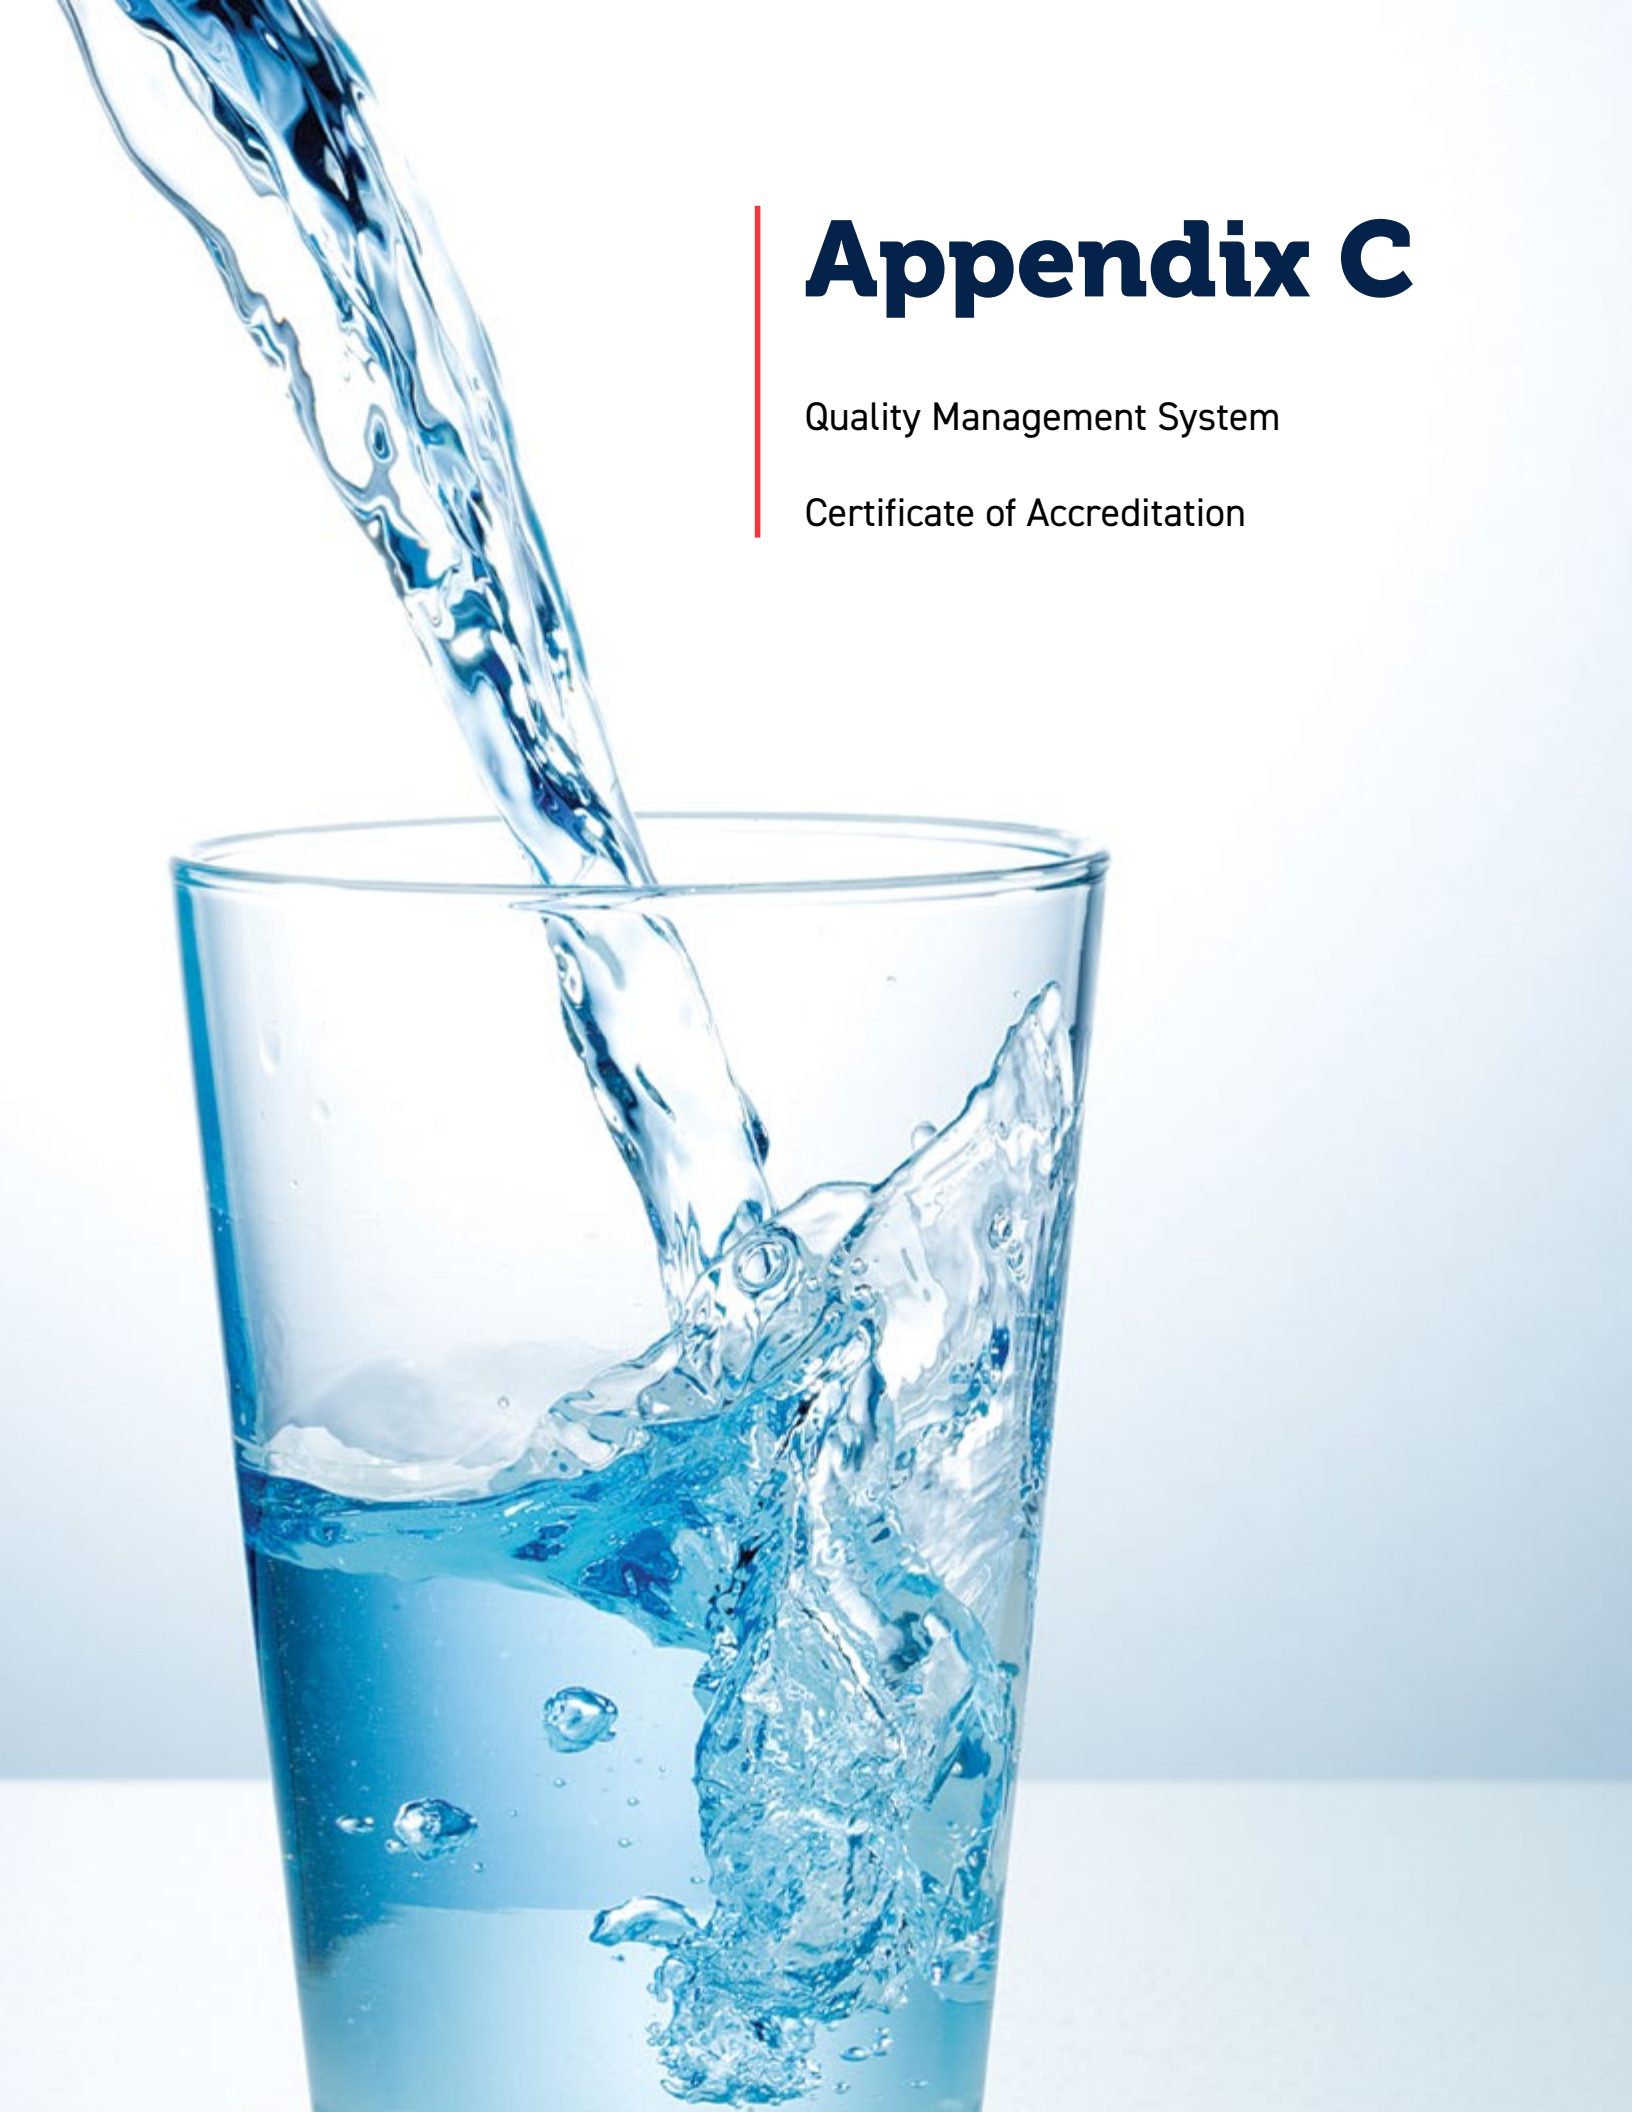

Appendix C

Quality Management System

Certificate of Accreditation

intertek SAI GLOBAL

CERTIFICATE OF ACCREDITATION

This is to certify that the following operating authority:

Town of Lincoln

4800 South Service Road, Beamsville, Ontario L0R 1B1, Canada

operates a Drinking Water System on behalf of

Town of Lincoln

4800 South Service Road, Beamsville, Ontario L0R 1B1, Canada

which conforms with the requirements of:

DRINKING WATER QUALITY MANAGEMENT STANDARD VERSION 2-2017

for the following scope of accreditation:

Drinking Water Treatment & Distribution; Full Scope

Including:

Beamsville Water Distribution System

Jordan-Vineland Distribution System

Certificate Number:
0202458

File No.:
2023-140894

Issue Date:
10 Jan. 2025

Original Certification Date:
20 Jan. 2016

Certification Effective Date:
09 Jan. 2025

Calin Moldovean
President Business Assurance

QMI-SAI Canada Ltd.
20 Carlson Court, Suite 200
Toronto, Ontario M9W 7K6 Canada

QMI-SAI Canada Ltd trading as Intertek and Intertek SAI Global, 20 Carlson Court, Suite 200, Toronto, Ontario M9W 7K6 Canada. This registration is subject to the INTERTEK SAI Global Terms and Conditions for Certification.
In the issuance of this certificate, INTERTEK SAI Global assumes no liability to any party other than to the Client, and then only in accordance with the agreed upon Certification Agreement. This certificate's validity is subject to the organization maintaining their system in accordance with INTERTEK SAI Global's requirements for systems certification. Validity may be confirmed via email at certificate.validation@intertek.com or by scanning the code to the right with a smartphone. The certificate remains the property of INTERTEK SAI Global, to whom it must be returned upon request
CT_DWQMS-2-SAIG-EN-LT-5.jan.24



Town of Lincoln

905.563.2799 | lincoln.ca
4800 South Service Rd., Beamsville, ON L3J 1L3
